Act ID	Description	Orig Dur	Rem Dur	Early Start
1000	Engineering Phase	7d	7d	01APR02 *
1010	Site Walk	0	0	01APR02 *
1015	SIte Photos	1d	1d	01APR02 *
1020	Preliminary Zoning Drawings	2d	2d	01APR02 *
1030	Title Work Ordered	0	0	02APR02 *
1040	Site Survey	2d	2d	02APR02 *
1050	Photo Simulations	1d	1d	01APR02 *
1060	Final Zoning Drawings	2d	2d	04APR02 *
1070	Zoning approval	0	0	12APR02 *
1073	Order Building	0	0	08APR02 *
1075	Order Geotech Report	0	0	04APR02 *
1080	Construciton Drawings	5d	5d	04APR02 *
1090	Submit to City For Plan Review	0	0	10APR02 *
1091	Complete & Distribute RFP	1d	1d	08APR02 *
1092	Bidding Period	7d	7d	09APR02 *
1093	Award Construction Contracts	0	0	18APR02 *
1100	Plan Approval / Permit Issuance	7d	7d	10APR02 *
1110	Utility Request	0	0	12APR02 *
1120	Telco Request	0	0	12APR02 *
1130	Construction Phase	14d2h	14d2h	18APR02 *
1140	Demo asphalt / Excavation	3d	3d	18APR02 *
1150	Power & Telco Underground Boring	4d	4d	23APR02 *
1151	Utility Inspections	1d	1d	26APR02 *
1160	Foundation Construction	5d	5d	29APR02 *
1161	Foundation Inspection	1d	1d	06MAY02 *
1171	Set Building	1d	1d	07MAY02 *
1181	Final Electrical Inspections	1d	1d	07MAY02 *
1191	Final Site Work / Landscaping	2d	2d	07MAY02 *
1201	Final Inspections	1d	1d	09MAY02 *
1211	Certificate of Occupancy / Facility Ready Date	0	0	

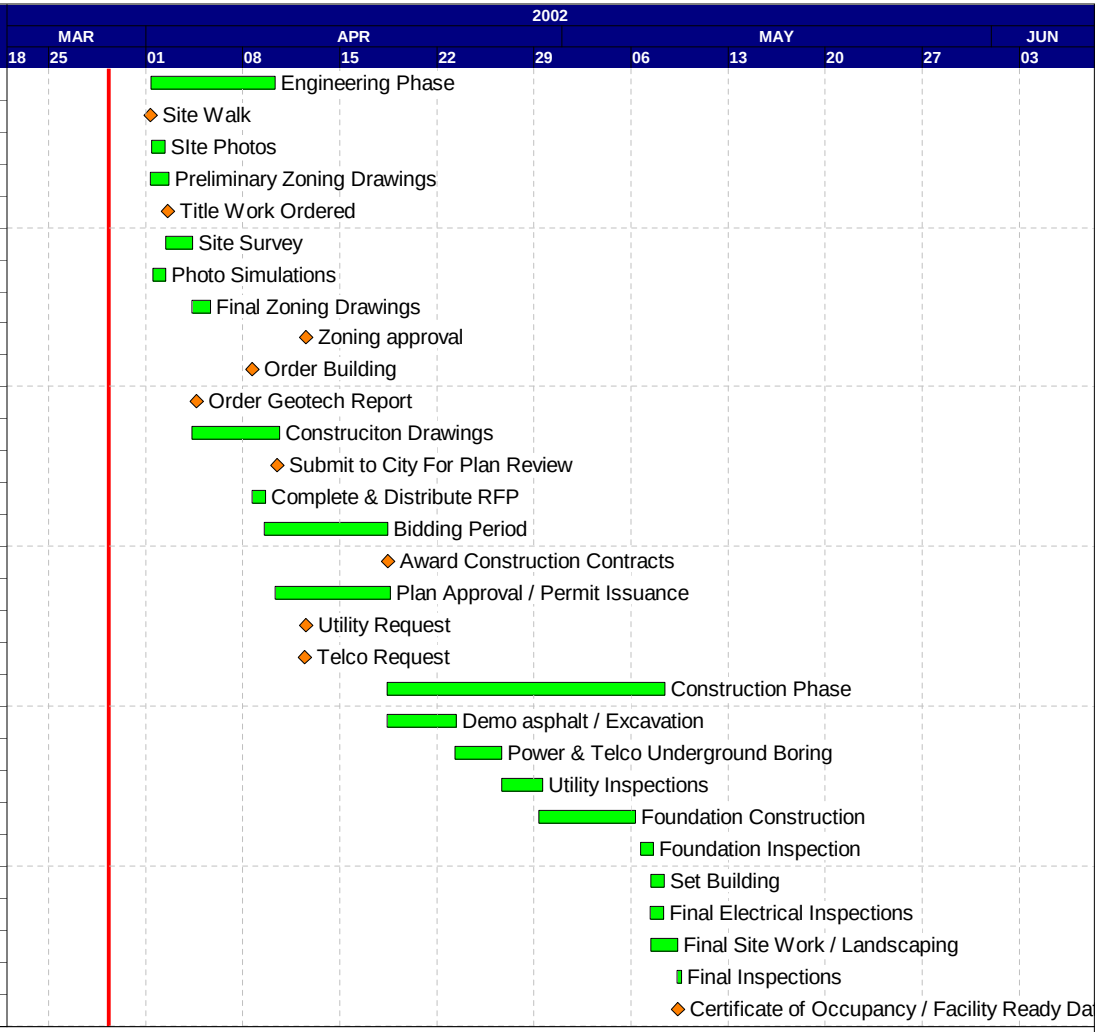

Start date	29MAR02
Finish date	09MAY02
Data date	29MAR02
Run date	29MAR02
Page number	1A

© Primavera Systems, Inc.

Millennium Venture Group
SAMPLE VoiceStream - Longmont #459

SUMMIT PROJECT DELIVERY SOLUTIONS INC.

MVG

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
